	Task Name	Unit	Duration	Start	Finish	% Complete
1	**NAME OF WORK: Restoration and Improvements of Balance main and cross roads of Nagenahalli , Harohalli , Kenchenahalli villages, Srinidhi layout, ISRO layout,KEB layout and surrounding areas in ward no -02. of yelahanka Sub division (PACKAGE NO-02)**					0%
2	**Work Order No : BBMP/EE/YNK.D/EPMT-08/W.O /111/21-22 Dated: 15-02-2022**					0%
3	**JOB NUMBER : 002-22-000003**					0%
4	**Name of Contractor: Sri.K.VENKATARAJU**					0%
5	Mobilization		10 days	Tue 15-02-22	Mon 28-02-22	100%
6	Removing & Refixing of Drain Covering Slabs	Sqm	25 days	Sun 20-02-22	Thu 24-03-22	0%
7	Earthwork Excavation of Drain Work	Cum	30 days	Fri 25-02-22	Thu 07-04-22	77%
8	Plain Cement Concrete of PCC 1:4:8	Cum	30 days	Mon 28-02-22	Fri 08-04-22	81%
9	TMT Steel	Tonne	35 days	Sat 05-03-22	Thu 21-04-22	79%
10	Reinforeced Cement Concrete M20	Cum	45 days	Thu 10-03-22	Wed 11-05-22	81%
11	100mm Precast Drain Covering Slab	Sqm	25 days	Fri 15-04-22	Thu 19-05-22	79%
12	230mm Culvert Slab	Sqm	25 days	Fri 15-04-22	Thu 19-05-22	73%
13	Plain Cement Concrete of PCC 1:3:6	Cum	25 days	Mon 25-04-22	Fri 27-05-22	0%
14	Precast Kerb Stone	Nos	25 days	Mon 25-04-22	Fri 27-05-22	100%
15	Dismantling of CC Pavement	Cum	20 days	Mon 18-04-22	Fri 13-05-22	12%

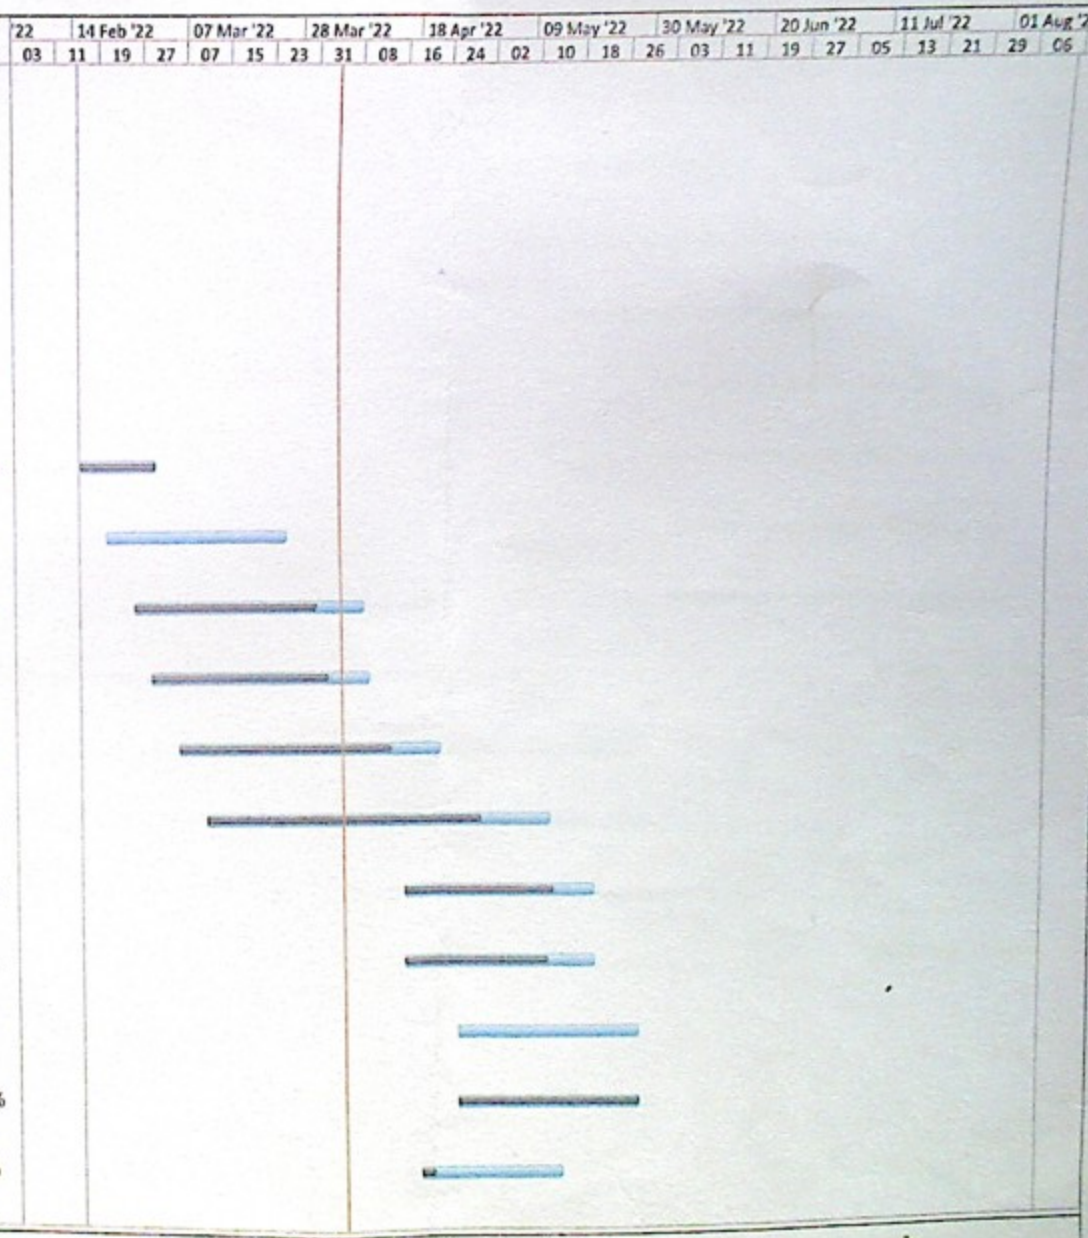

Project: Project-02, Bar Chart
Date: Mon 04-04-22

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ,
ಜ.ಜ.ಎ.ಪಿ. ಬೆಂಗಳೂರು-೧೦೬

	Task Name	Unit	Duration	Start	Finish	% Complete
16	Earth Work Excavation for Road Work	Cum	35 days	Mon 25-04-22	Fri 10-06-22	80%
17	Camapaction of original ground	Sqm	35 days	Sat 30-04-22	Thu 16-06-22	70%
18	Granular Sub Base	Cum	45 days	Thu 05-05-22	Wed 06-07-22	86%
19	Wet Mix Macadam	Cum	45 days	Sun 15-05-22	Thu 14-07-22	80%
20	Primer Coat	Sqm	45 days	Wed 01-06-22	Tue 02-08-22	81%
21	Dense Graded Bitumious Macadam	Cum	45 days	Thu 02-06-22	Wed 03-08-22	81%
22	Tack Coat	Sqm	45 days	Fri 03-06-22	Thu 04-08-22	81%
23	Bitumious Concrete	Cum	45 days	Sat 04-06-22	Thu 04-08-22	81%
24	Lane Marking	Sqm	25 days	Mon 11-07-22	Fri 12-08-22	38%
25	Dry Lean Cement Concrete	Cum	20 days	Tue 05-07-22	Mon 01-08-22	10%
26	Cement Concrete Pavement	Cum	20 days	Sun 10-07-22	Thu 04-08-22	10%
27	Pavement Markers or Studds	Nos	25 days	Mon 11-07-22	Fri 12-08-22	0%
28	Kerb Painting	Sqm	25 days	Mon 11-07-22	Fri 12-08-22	99%

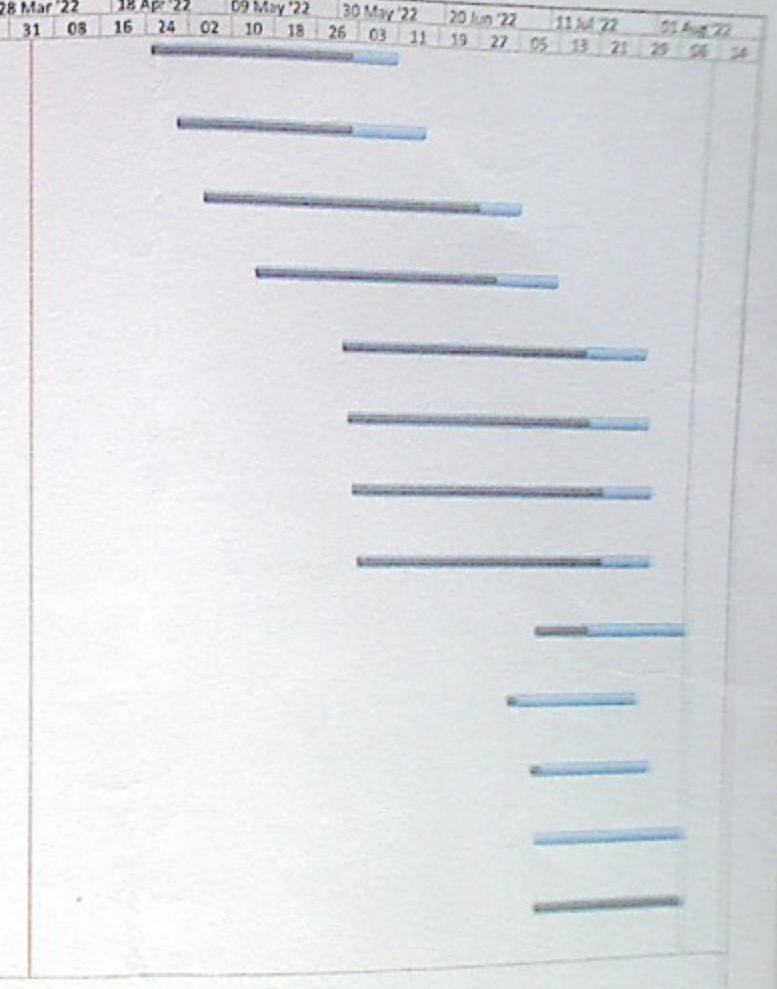

Project: Project-02, Bar Chart
Date: Mon 04-04-22

Task | Split | Milestone | Summary
Project Summary | External Tasks | External Milestone | Inactive Task
Inactive Milestone | Inactive Summary | Manual Task | Duration-only
Manual Summary Rollup | Manual Summary | Start-only | Finish-only
Deadline | Progress

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಧಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ,
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-೫೯

	Task Name	Unit	Duration	Start	Finish	% Complete
1	**Name of the work : Restoration and Improvements of Roads at Hesaraghatta Main road, G Ramaiah layout, Sai Archade layout, Vijaya bank layout, Adityanagara Phase-02, and Surrounding areas in ward no-03 of Yelahanka New town Sub-division**					0%
2	**Name of Agency: Sri K Venkataraju.**					0%
3	**Work Order No: BBMP/EE/YNK.D/EPMT-08/W.O/ Date: 15.02.2022**					0%
4	Mobilization		10 days	Tue 15-02-22	Mon 28-02-22	100%
5	Earthwork Excavation for Drain Work	Cum	25 days	Sun 20-02-22	Thu 24-03-22	85%
6	Plain Cement Concrete 1:4:8	Cum	35 days	Fri 25-02-22	Thu 14-04-22	89%
7	TMT Steel	Tonne	35 days	Sat 05-03-22	Thu 21-04-22	80%
8	Reinforeced Cement Concrete M20	Cum	40 days	Thu 10-03-22	Wed 04-05-22	85%
9	100mm Precast Covering Slabs	Sqm	35 days	Fri 25-03-22	Thu 12-05-22	92%
10	230mm Culvert Covering Slab	Sqm	35 days	Fri 25-03-22	Thu 12-05-22	54%
11	Plain Cement Concrete 1:3:6	Cum	35 days	Mon 28-03-22	Fri 13-05-22	92%
12	Pre Cast Kerb	Nos	45 days	Mon 28-03-22	Fri 27-05-22	100%
13	Earthwork Excavation for Road Work	Cum	35 days	Tue 15-03-22	Mon 02-05-22	12%
14	Compaction of original ground	Sqm	35 days	Sun 20-03-22	Thu 05-05-22	11%

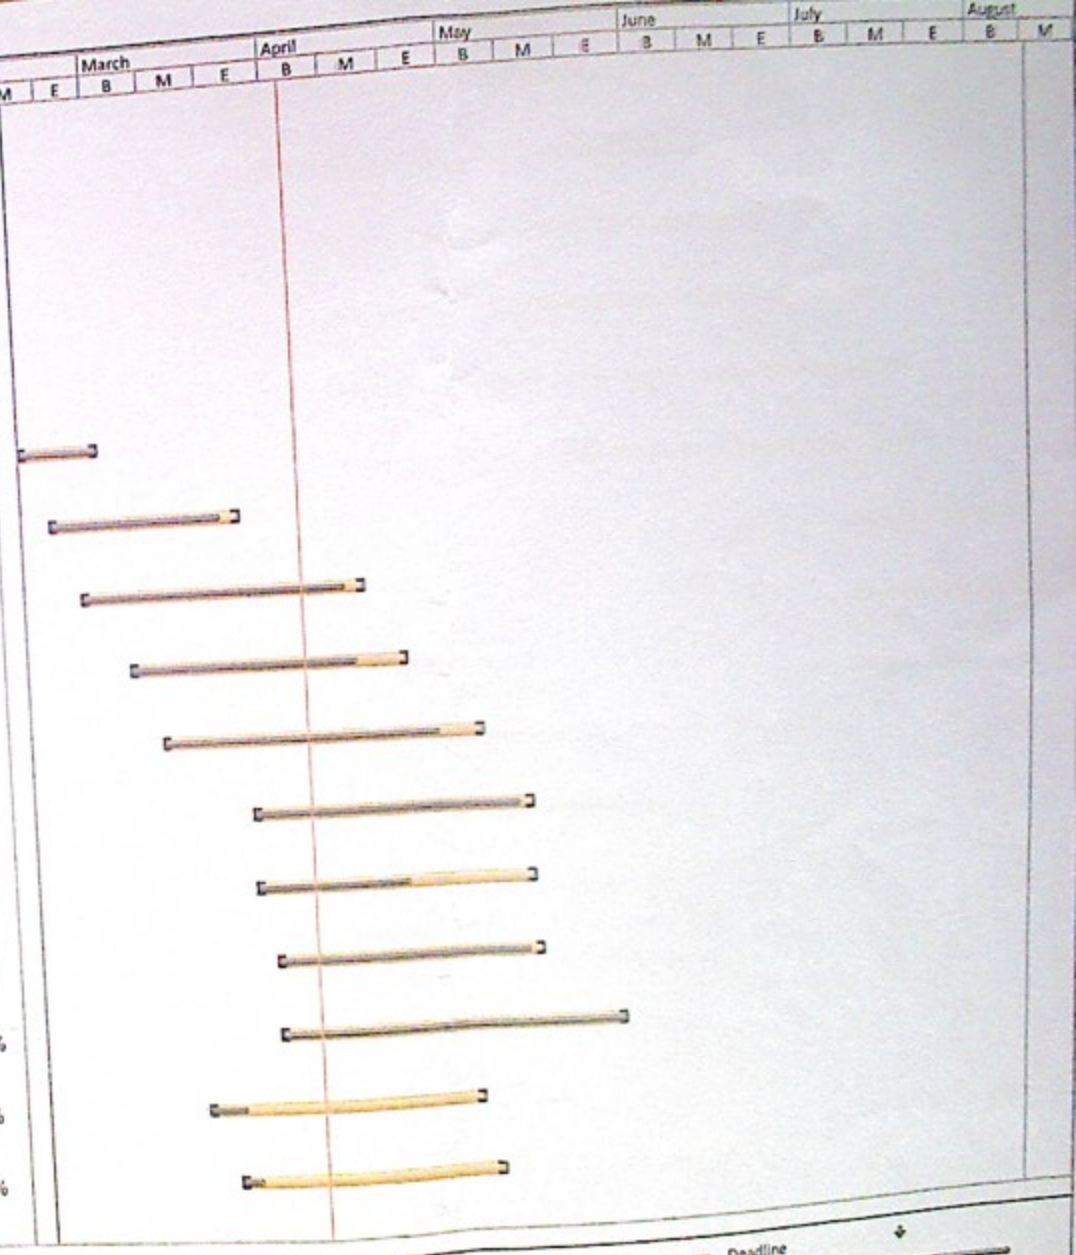

Project: Package-09, Bar Chart
Date: Mon 04-04-22

Task
Split
Milestone
Summary

Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ.
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-೬೪

	Task Name	Unit	Duration	Start	Finish	% Complete
15	Granular Sub Base	Cum	50 days	Fri 25-03-22	Thu 02-06-22	15%
16	Wet Mix Mecadam	Cum	50 days	Wed 30-03-22	Tue 07-06-22	15%
17	Primer Coat	Sqm	55 days	Sun 10-04-22	Thu 23-06-22	15%
18	Dense Graded Bituminous Macadam	Cum	70 days	Mon 11-04-22	Fri 15-07-22	15%
19	Tack Coat	Sqm	70 days	Tue 12-04-22	Mon 18-07-22	15%
20	Bitumious Concrete	Cum	70 days	Wed 13-04-22	Tue 19-07-22	15%
21	Lane Marking	Sqm	25 days	Sun 10-07-22	Thu 11-08-22	0%
22	Pavement Markers or Studds	Nos	25 days	Sun 10-07-22	Thu 11-08-22	0%
23	Kerb Painting	Sqm	30 days	Fri 01-07-22	Thu 11-08-22	93%

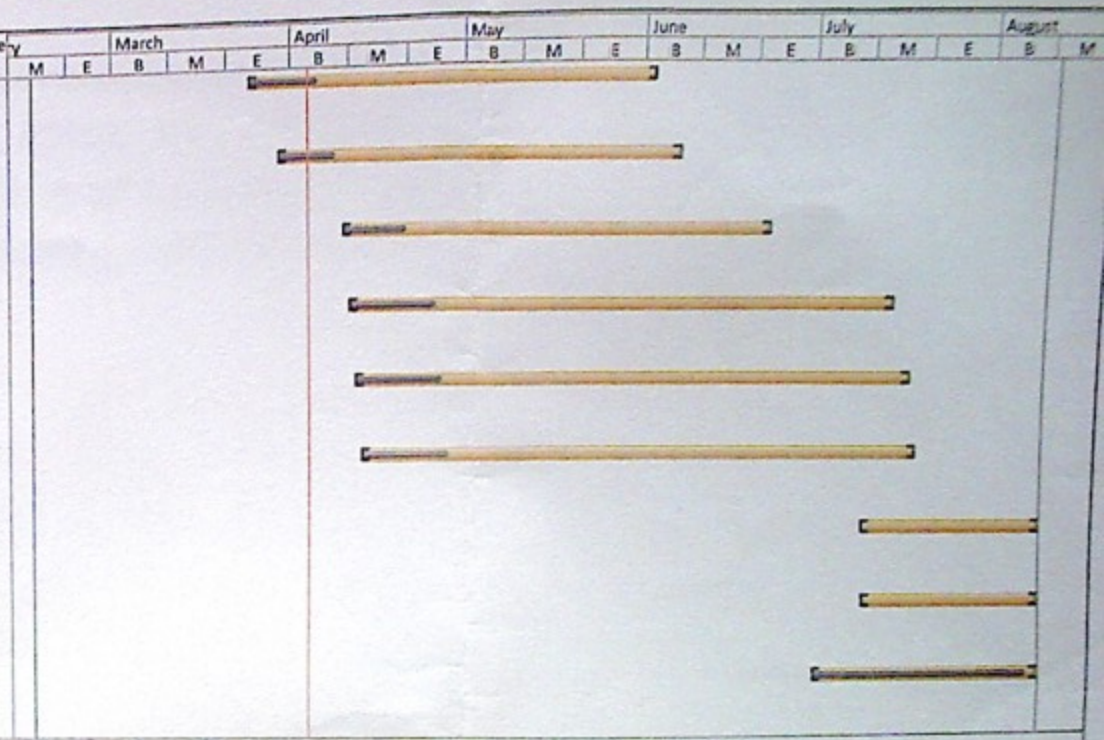

Project: Package-09, Bar Chart
Date: Mon 04-04-22

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ,
ಜಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-106
